

DOST-STII

STARBOOKS: WHIZ CHALLENGE



TEAM NEXUS

Project Management

PROJMAN – SF 231

Term 3 A.Y. 2025–2026

Mr. Jose Eugenio L. Quesada

Our Team



Kelly Dumbrique



Arcielle Marie Gercan



Shandrae Lois Quianzon



Janice Maxene Salipande



Mr. Jose Eugenio L. Quesada
Project Adviser

PMBOK Documents



Shandrae Quianzon

NEXUS Sharepoint

Documents > 4 - PROJMAN > PROJMAN Finals Documentation

+ New

Upload

Edit in grid view

Share

Copy link

...

All Documents

	Name	Modified	Modified By
	01 Initiation	23 minutes ago	Janice Maxene Salipai
	02 Planning	23 minutes ago	Janice Maxene Salipai
	03 Execution	23 minutes ago	Janice Maxene Salipai
	04 Monitoring and Controlling	23 minutes ago	Janice Maxene Salipai
	05 Closing	23 minutes ago	Janice Maxene Salipai
	06 Agile	23 minutes ago	Janice Maxene Salipai
	07 Project Documents	23 minutes ago	Janice Maxene Salipai
	PROJMAN Finals Documentation.docx	23 minutes ago	Janice Maxene Salipai
	PROJMAN Finals Documentation.pdf	23 minutes ago	Janice Maxene Salipai

APC_2025_2026_T1_MI232_G06 NEXUS DOST: STARBOOKS Whiz Challenge

Wiki

01 Initiation | PMBOK Project Management Phases (Waterfall)

02 Planning | PMBOK Project Management Phases (Waterfall)

03 Execution | PMBOK Project Management Phases (Waterfall)

04 Monitoring and Controlling | PMBOK Project Management Phases (Waterfall)

05 Closing | PMBOK Project Management Phases (Waterfall)

06 Agile | PMBOK Project Management Phases (Waterfall)

07 Project Documents | PMBOK Project Management Phases (Waterfall)

OpenProject Wiki

APC_2025_2026_T1_MI232_G06-DOST-STARBOOKS-Whiz-Challenge- / docs / PROJMAN / PROJMAN Finals Documentation /

 jdsalipande2

Add files via upload

Name	Last commit message
 ..	
 01 Initiation	Add files via upload
 02 Planning	Add files via upload
 03 Execution	Add files via upload
 04 Monitoring and Controlling	Add files via upload
 05 Closing	Add files via upload
 06 Agile	Add files via upload
 07 Project Documents	Add files via upload
 PROJMAN Finals Documentation.docx	Add files via upload
 PROJMAN Finals Documentation.pdf	Add files via upload

GitHub Repo

Sprint Ceremonies



Kelly Dumbrique

For Term 3 A.Y. 2025–2026:

Sprint 6

March 23 – April 3

Sprint 7

April 13 – April 24

Sprint 8

April 27 – May 8

Sprint 6 Ceremonies

Sprint Planning Meeting (March 20)

[illegible]

Focus:

Improved UI and optimized existing features
Continued development of admin-side functionalities

Sprint 6 Ceremonies

Daily Standup Meeting (every Tue and Fri)

 Janice Maxene Salipande 3/23 7:05 PM

 **Day 01 Daily Scrum (every Tuesday)** ↻
Occurs every Tuesday 9:00 AM

Scheduled a meeting



[See details](#)

 Reply

 Janice Maxene Salipande 3/23 7:07 PM

 **Day 02 Daily Scrum (every Friday)** ↻
Occurs every Friday 1:00 PM

Scheduled a meeting



[See details](#)

 Reply

[Sprint 06 Day 04 Daily Scrum Meeting Individual Updated Report](#)

[Sprint 06 Day 03 Daily Scrum Meeting Individual Updated Report](#)

[Sprint 06 Day 02 Daily Scrum Meeting Individual Updated Report](#)

[Sprint 06 Day 01 Daily Scrum Meeting Individual Updated Report](#)

Sprint 6 Ceremonies

Backlog Refinement Meeting (April 9)



Sprint 6 Ceremonies

Sprint Review Meeting (April 8)



Feedback:

Actual kiosk specifications were different from the device introduced during MNTSDEV
Encountered device specs misalignment
Optimized code and system performance for compatibility

Sprint 6 Ceremonies

Sprint Retrospective Meeting (April 9)

The screenshot displays a digital tool for a Sprint Retrospective meeting. It is titled "Sprint 6 Retrospective" and includes a header with a "Ready?" toggle (0/3) and a search bar. The interface is divided into three main columns, each with a header and a list of items.

- Glad (Positive experiences):**
 - Initial deployment is successful (Janice Salipande, 0 votes)
 - Project almost finished and on track (Arielle Marie Gercan, 4 votes)
 - client is happy with our progress (Janice Salipande, 0 votes)
- Sad (Negative experiences):**
 - Code errors (Kelly Dumbrique, 0 votes)
 - Specs of device do not match with the group's c (Kelly Dumbrique, 4 votes)
- Mad (Frustrations and challenges):**
 - Docker will not be used (Kelly Dumbrique, 2 votes)
 - Code errors during deployment (Janice Salipande, 2 votes)
 - Client's requirements are always changing (Janice Salipande, 0 votes)

Each item includes a user profile picture, a description, and a voting interface with a minus, plus, and reset button. There are also "Add Item" buttons at the bottom of each column.

Action Items:

- Maintain current workflow and task distribution to ensure timely completion
- Refactor and optimize the system to fit the lower/actual device constraints
- Create a step-by-step deployment guide
- Perform compatibility testing early before final deployment

Sprint 7 Ceremonies

Sprint Planning Meeting (April 9)



Sprint 7 Planning Meeting
April 9, 2026 Expires in 1556 days • 9 views • SharePoint App • HD • ... > GDS NDRUS > Recordings

APC_2025_2026_T1_M1232_G0... / Boards / Public: AY 2025-2026 T3 Sprin...

AY 2025-2026 T3 Sprint 07

Committed Backlog Items	Tasks Assigned (Not Started)	In Progress	For Review/Testing	Reviewed/Tested	Done
Closed #6050 - APC_2025_2026_T1... USER STORY 3.3.6.6.3 As an admin, I want to upload a CSV file containing multiple questions so that I can quickly add large sets of questions into the system without entering them manually. Apr 13, 2026 - Apr 24, 2026					Closed #6042 - APC_2025_2026_T1... USER STORY 3.3.5.1.3 As a player, I want the system to read the question aloud before the timer starts so that I can better understand the question. Apr 13, 2026 - Apr 24, 2026
Closed #6042 - APC_2025_2026_T1... USER STORY 3.3.5.1.3 As a player, I want the system to read the question aloud before the timer starts so that I can better understand the question. Apr 13, 2026 - Apr 24, 2026					Closed #5159 - APC_2025_2026_T1... USER STORY 3.3.3.1 As a player, I want to view my profile section on the homepage so I can see my avatar, stars, badges, and progress. Apr 13, 2026 - Apr 24, 2026
Closed #6055 - APC_2025_2026_T1... USER STORY 3.3.6.6.4 As an admin, I want to select all questions using a single checkbox so that I can quickly perform bulk actions without selecting each question individually. Apr 13, 2026 - Apr 24, 2026					Closed #5182 - APC_2025_2026_T1... USER STORY 3.3.6.6.1 As an admin, I want to view a list of all quiz questions so I can monitor and manage the content. Apr 13, 2026 - Apr 24, 2026
Closed #5159 - APC_2025_2026_T1... USER STORY 3.3.3.1 As a player, I want to view my profile section on the homepage so I can see my avatar, stars, badges, and progress. Apr 13, 2026 - Apr 24, 2026					Closed #5183 - APC_2025_2026_T1... USER STORY 3.3.6.6.2 As an admin, I want to add new quiz questions so I can expand the content for players. Apr 13, 2026 - Apr 24, 2026
Closed #5182 - APC_2025_2026_T1... USER STORY 3.3.6.6.1 As an admin, I want to view a list of all quiz questions so I can monitor and manage the content. Apr 13, 2026 - Apr 24, 2026					Closed #6050 - APC_2025_2026_T1... USER STORY 3.3.6.6.3 As an admin, I want to upload a CSV file containing multiple questions so that I can quickly add large sets of questions into the system without entering them manually. Apr 13, 2026 - Apr 24, 2026
Closed #5183 - APC_2025_2026_T1... USER STORY 3.3.6.6.2 As an admin, I want to add new quiz questions so I can expand the content for players. Apr 13, 2026 - Apr 24, 2026					Closed #6055 - APC_2025_2026_T1... USER STORY 3.3.6.6.4 As an admin, I want to select all questions using a single checkbox so that I can quickly perform bulk actions without selecting each question individually. Apr 13, 2026 - Apr 24, 2026

Focus:

- Text-to-Speech feature for Whiz Challenge
- Bulk selection feature in Questions menu in admin
- Continue admin panel polishing

Sprint 7 Ceremonies

Daily Standup Meeting (every Tue and Fri)

 Janice Maxene Salipande 3/23 7:05 PM

 **Day 01 Daily Scrum (every Tuesday)** ↻
Occurs every Tuesday 9:00 AM

Scheduled a meeting



[See details](#)

 Reply

 Janice Maxene Salipande 3/23 7:07 PM

 **Day 02 Daily Scrum (every Friday)** ↻
Occurs every Friday 1:00 PM

Scheduled a meeting



[See details](#)

 Reply

[Sprint 07 Day 04 Daily Scrum Meeting Individual Updated Report](#)

[Sprint 07 Day 03 Daily Scrum Meeting Individual Updated Report](#)

[Sprint 07 Day 02 Daily Scrum Meeting Individual Updated Report](#)

[Sprint 07 Day 01 Daily Scrum Meeting Individual Updated Report](#)

Sprint 7 Ceremonies

Backlog Refinement Meeting (April 24)




Sprint 7 Ceremonies

Sprint Review Meeting (May 4)



Sprint 7 Ceremonies

Sprint Retrospective Meeting (April 24)

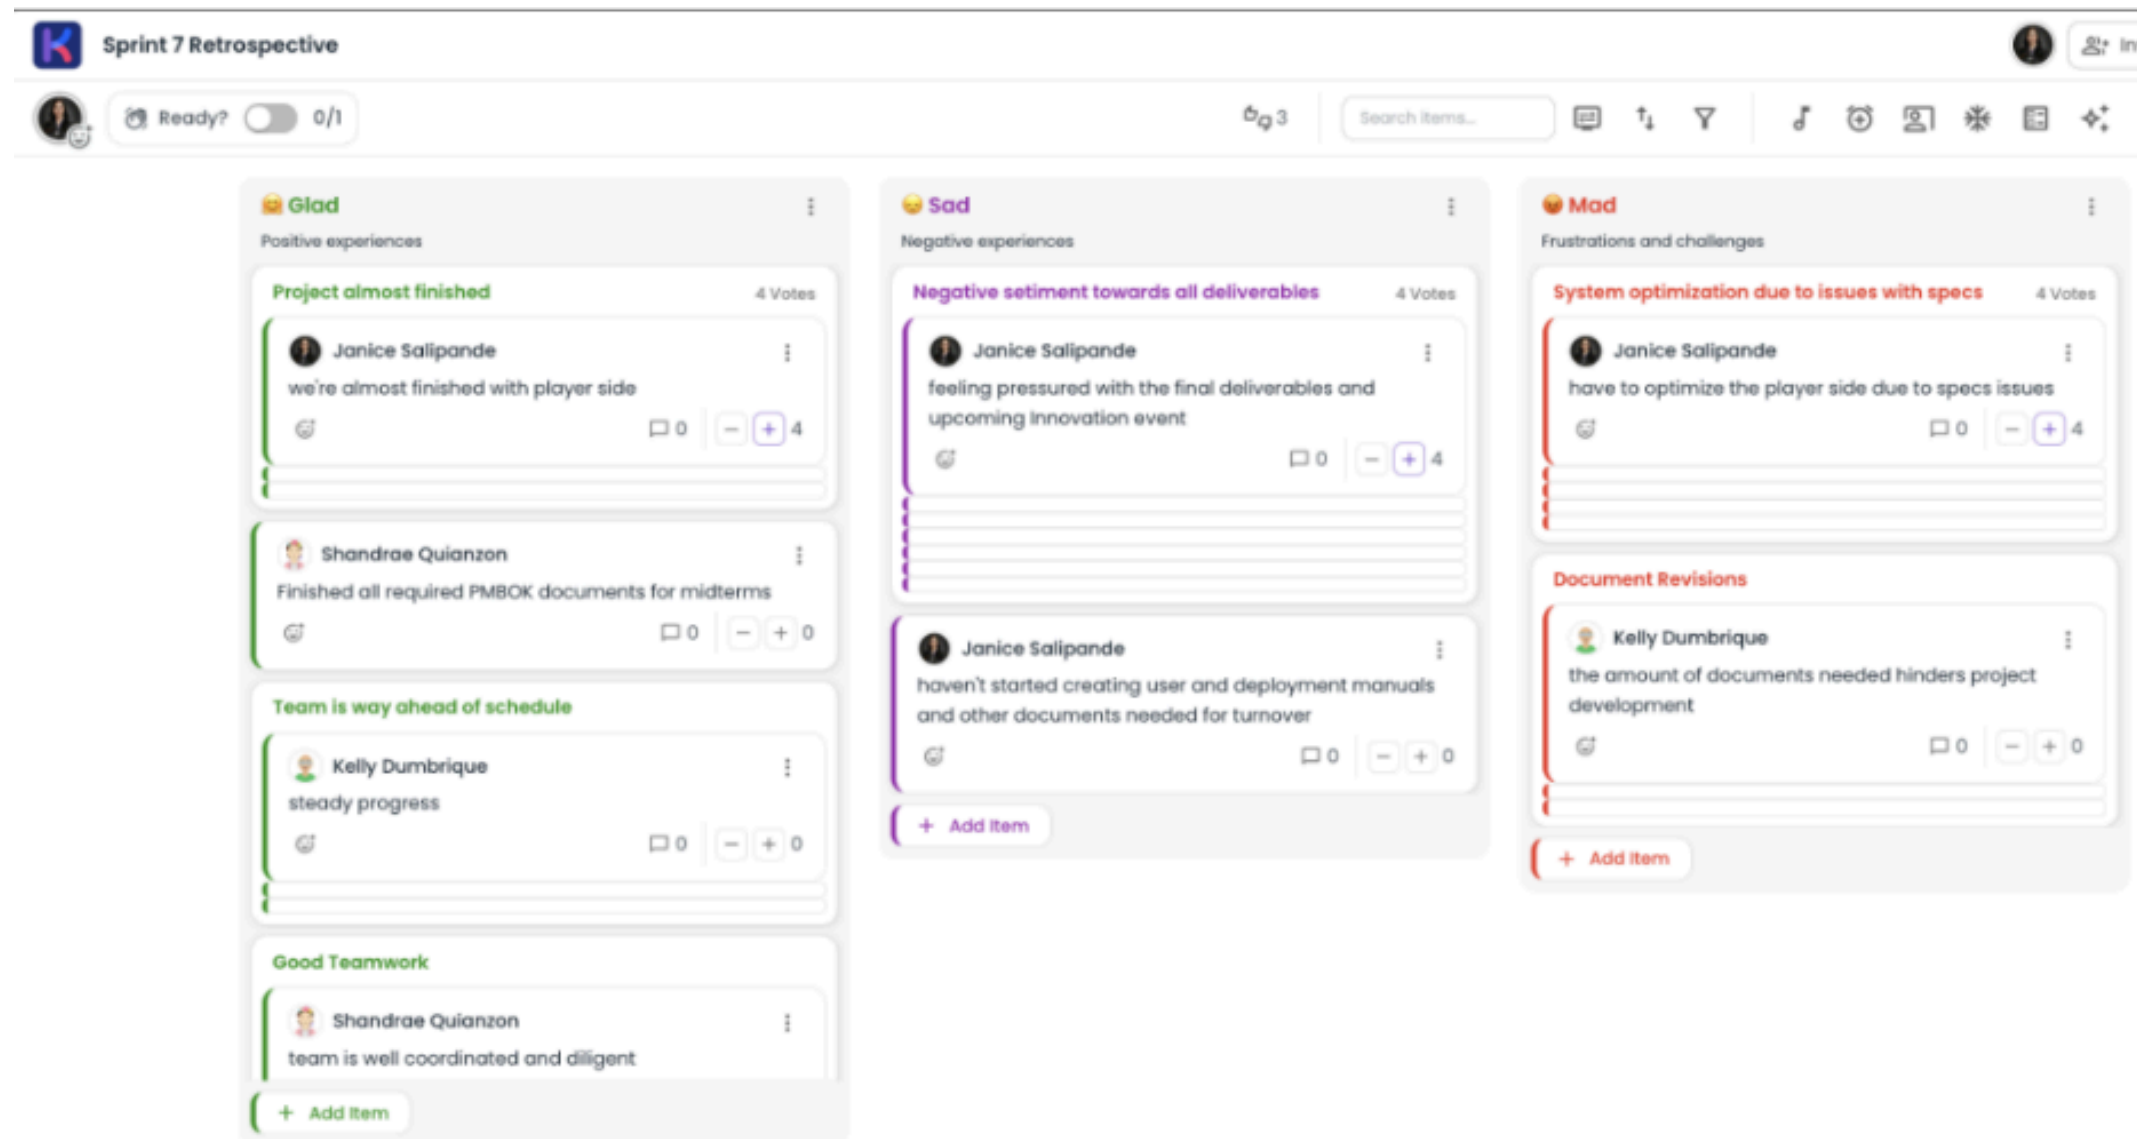


Action Items:

- Set realistic daily/short-term goals instead of focusing only on final deadlines
- Align all remaining development with specs constraints
- Redistribute tasks to ensure balanced workload across members
- Prioritize high-impact tasks only and there should be no new features unless critical

Sprint 8 Ceremonies

Sprint Planning Meeting (April 24)

APC_2025_2026_T1_M1232_G0... / Boards / Public: AY 2025-2026 T3 Sprint...
AY 2025-2026 T3 Sprint 08

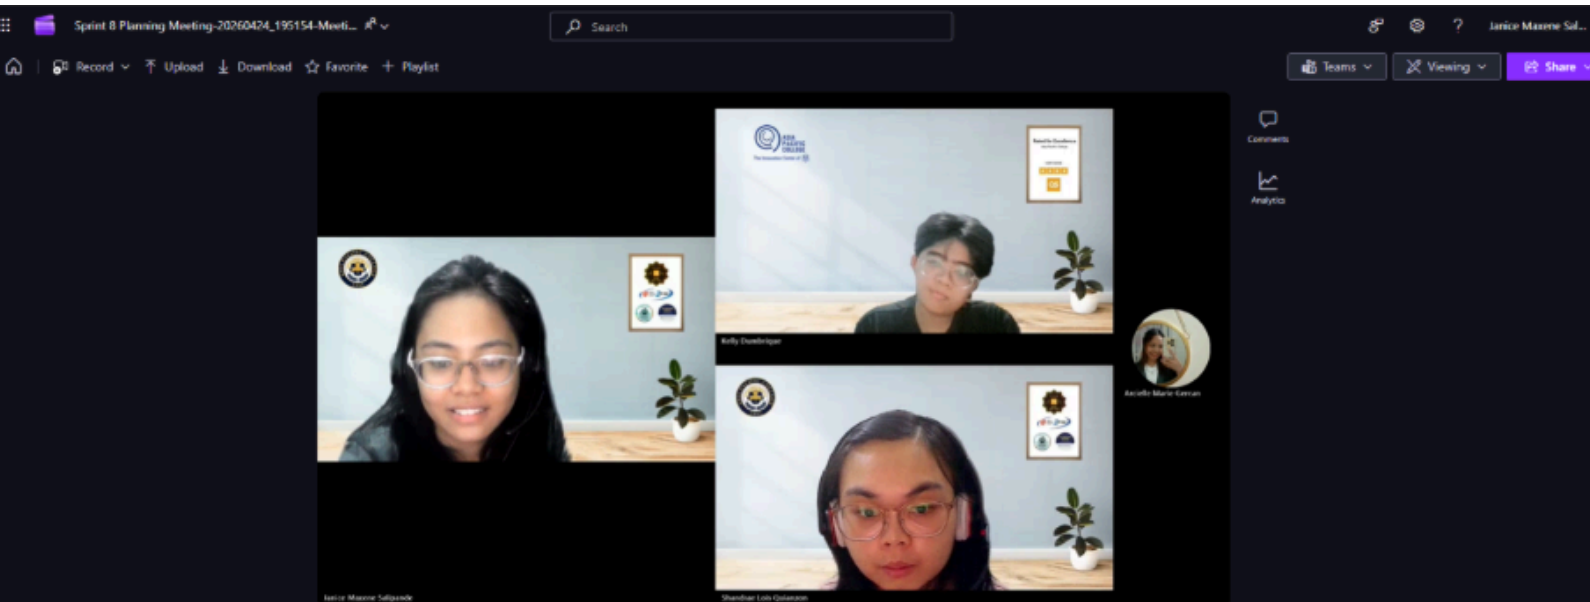

Sprint 8 Planning Meeting
 April 24, 2026 Expires in 1972 days • 7 views • SharePoint App • HD • ... • GUS NEXUS • Recordings

Committed Backlog Items	Tasks Assigned (Not Started)	In Progress	For Review/Testing	Reviewed/Tested	Done
+ Closed #6042 - APC_2025_2026_T1... USER STORY 1.5 Business Model Canvas Apr 27, 2026 - May 13, 2026					+ Closed #6042 - APC_2025_2026_T1... USER STORY 1.5 Business Model Canvas Apr 27, 2026 - May 13, 2026
+ Closed #6056 - APC_2025_2026_T1... USER STORY 1.6 Feasibility Study Apr 27, 2026 - May 13, 2026					+ Closed #6056 - APC_2025_2026_T1... USER STORY 1.6 Feasibility Study Apr 27, 2026 - May 13, 2026
+ Closed #6048 - APC_2025_2026_T1... USER STORY 2.5.02 Risk Management Plan Apr 27, 2026 - May 08, 2026					+ Closed #6048 - APC_2025_2026_T1... USER STORY 2.5.02 Risk Management Plan Apr 27, 2026 - May 08, 2026
+ Closed #6054 - APC_2025_2026_T1... USER STORY 2.5.06 Requirements Management Plan Apr 27, 2026 - May 08, 2026					+ Closed #6054 - APC_2025_2026_T1... USER STORY 2.5.06 Requirements Management Plan Apr 27, 2026 - May 08, 2026
+ Closed #6049 - APC_2025_2026_T1... USER STORY 2.5.07 Risk Register Apr 27, 2026 - May 08, 2026					+ Closed #6049 - APC_2025_2026_T1... USER STORY 2.5.07 Risk Register Apr 27, 2026 - May 08, 2026
+ Closed #6050 - APC_2025_2026_T1... USER STORY 2.5.10 Configuration Management Plan Apr 27, 2026 - May 08, 2026					+ Closed #6050 - APC_2025_2026_T1... USER STORY 2.5.10 Configuration Management Plan Apr 27, 2026 - May 08, 2026
+ Closed #6051 - APC_2025_2026_T1... USER STORY 2.5.11 Change Management Plan Apr 27, 2026 - May 08, 2026					+ Closed #6051 - APC_2025_2026_T1... USER STORY 2.5.11 Change Management Plan Apr 27, 2026 - May 08, 2026
+ Closed #6058 - APC_2025_2026_T1... USER STORY 4.6.1 Project Status Report (Sprint 07) Apr 27, 2026 - May 08, 2026					+ Closed #6058 - APC_2025_2026_T1... USER STORY 4.6.1 Project Status Report (Sprint 07)

Focus:

Player-Side Optimization

PMBOK Documents

Sprint 8 Ceremonies

Daily Standup Meeting (every Tue and Fri)

 Janice Maxene Salipande 3/23 7:05 PM

 **Day 01 Daily Scrum (every Tuesday)** ↻
Occurs every Tuesday 9:00 AM

Scheduled a meeting



[See details](#)

 Reply

 Janice Maxene Salipande 3/23 7:07 PM

 **Day 02 Daily Scrum (every Friday)** ↻
Occurs every Friday 1:00 PM

Scheduled a meeting



[See details](#)

 Reply

[Sprint 08 Day 04 Daily Scrum Meeting Individual Updated Report](#)

[Sprint 08 Day 03 Daily Scrum Meeting Individual Updated Report](#)

[Sprint 08 Day 02 Daily Scrum Meeting Individual Updated Report](#)

[Sprint 08 Day 01 Daily Scrum Meeting Individual Updated Report](#)

Sprint 8 Ceremonies

Sprint Review Meeting (May 13)




Feedback:

- Ensure Whiz Battle functionality across multiple devices
- Optimize player-side for mobile device compatibility
- Develop a complete admin dashboard (analytics and leaderboard)
- Finalize and revise all documentation for system turnover

Sprint 8 Ceremonies

Sprint Retrospective Meeting (May 13)

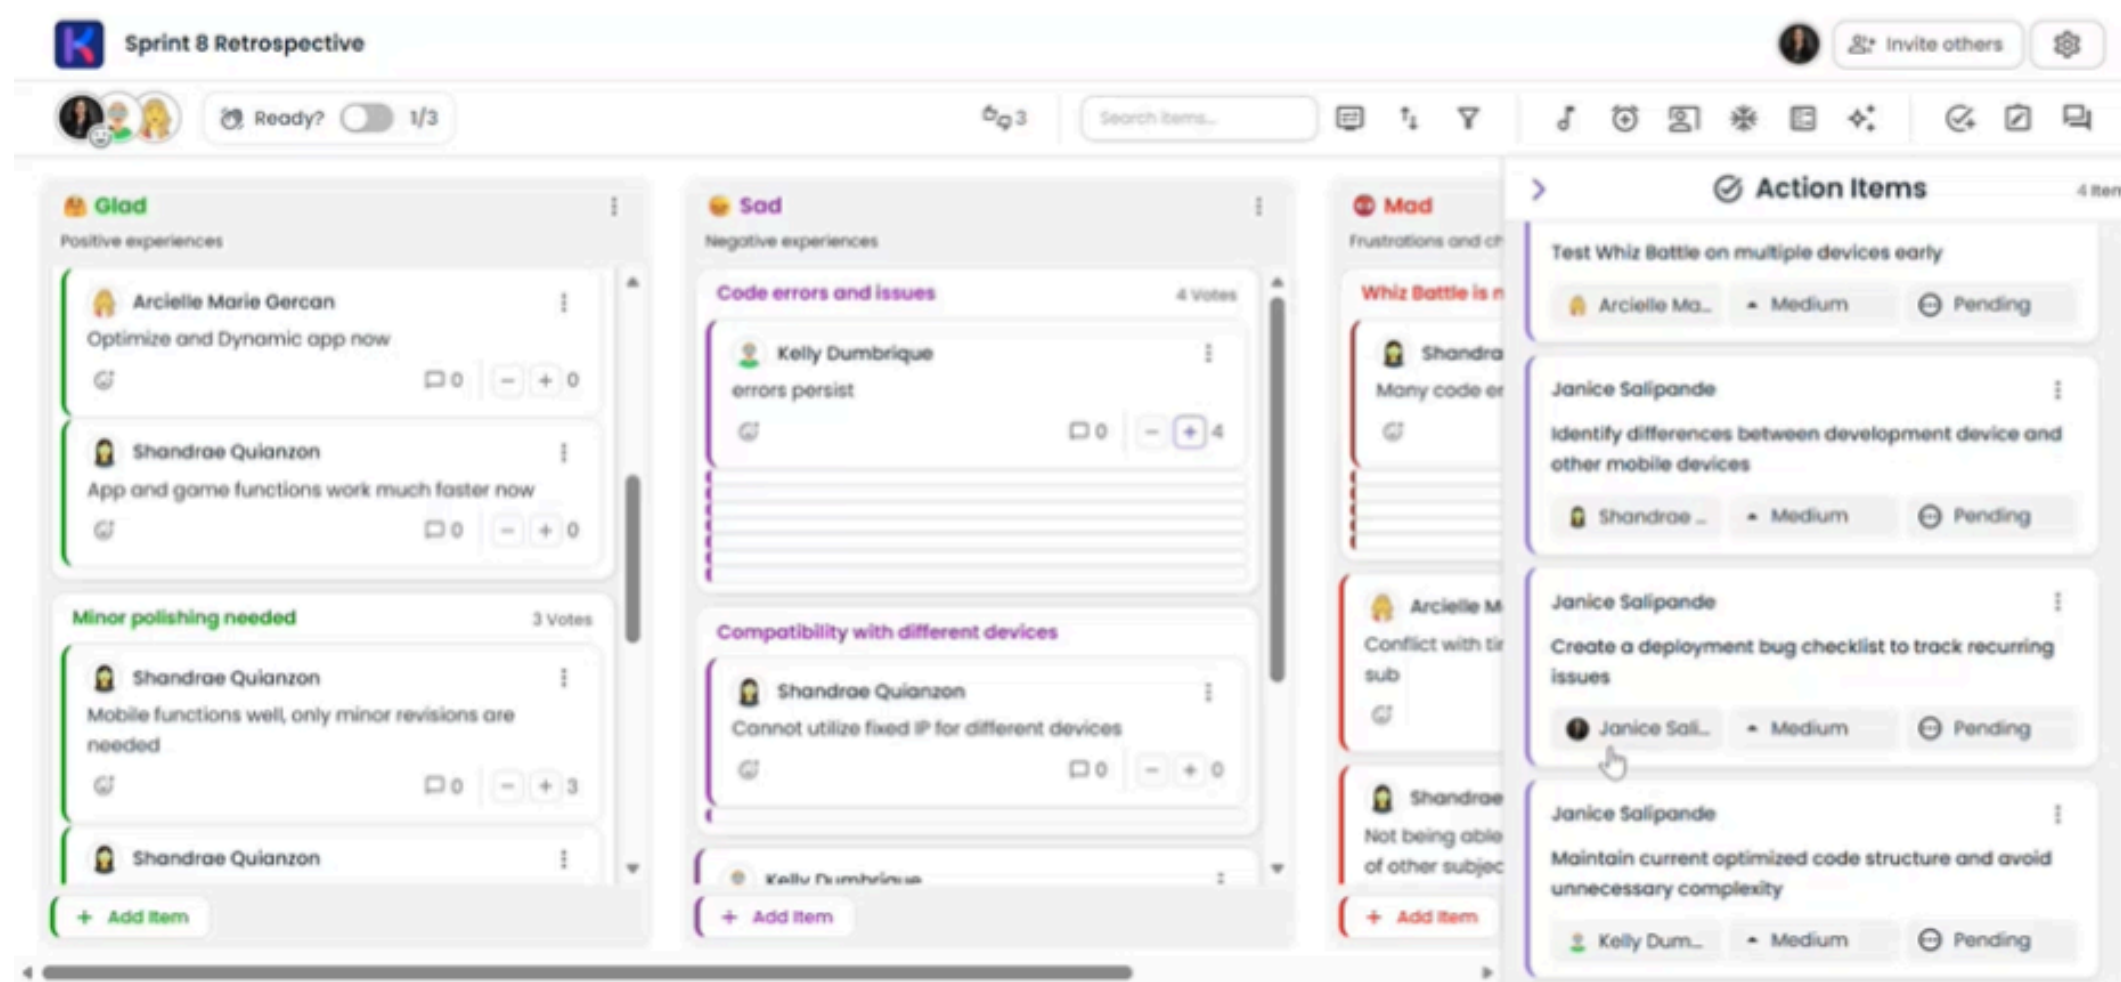

Action Items:

- Test Whiz Battle on multiple devices early
- Identify differences between development device and other mobile devices
- Create a deployment bug checklist to track recurring issues
- Maintain current optimized code structure and avoid unnecessary complexity

OpenProject



Janice Salipande

Sprint Budget Summary

Sprint	PV	EV	AC	CV	CPI	SPI	Status
Sprint 6	100,000	90,000	46,500	43,500	1.94	0.9	Under budget
Sprint 7	100,000	95,000	32,500	62,500	2.92	0.95	Under budget
Sprint 8	100,000	100,000	13,000	87,000	7.69	1	Under budget

System Demo



Arcielle Gercan

Individual Contributions



Kelly Dumbrique

Team Leader, Product Owner, Developer

- Coordinated and facilitated meetings with the adviser and client
- Developed/polished/optimized the frontend interface for the Whiz Battle game mode, Admin Management, Question Management, and Difficulty Settings
- Completed Requirements Management Plan, Change Management Plan, Project Acceptance, and Post Project Review documents



Arcielle Marie Gercan

Lead Developer

- Polished/optimized the frontend interface for all modules and components while ensuring backend services function properly across the system.
- Completed Business Model Canvas, and Configuration Management Plan documents



Shandrae Lois Quianzon

Lead Developer

- Developed/polished/optimized the frontend interface for the Whiz Challenge game mode, and Leaderboard
- Completed Risk Management Plan, Risk Register, and Transition Out Plan documents



Janice Maxene Salipande

Scrum Master, Developer, Lead Tester

- Developed/polished/optimized the frontend interface for the Whiz Puzzle game mode, Player Management, Analytics, and Leaderboard
- Completed Feasibility Study, Project Status Reports, and Lessons Learned documents

Thank you!



how it started



how it's going
